


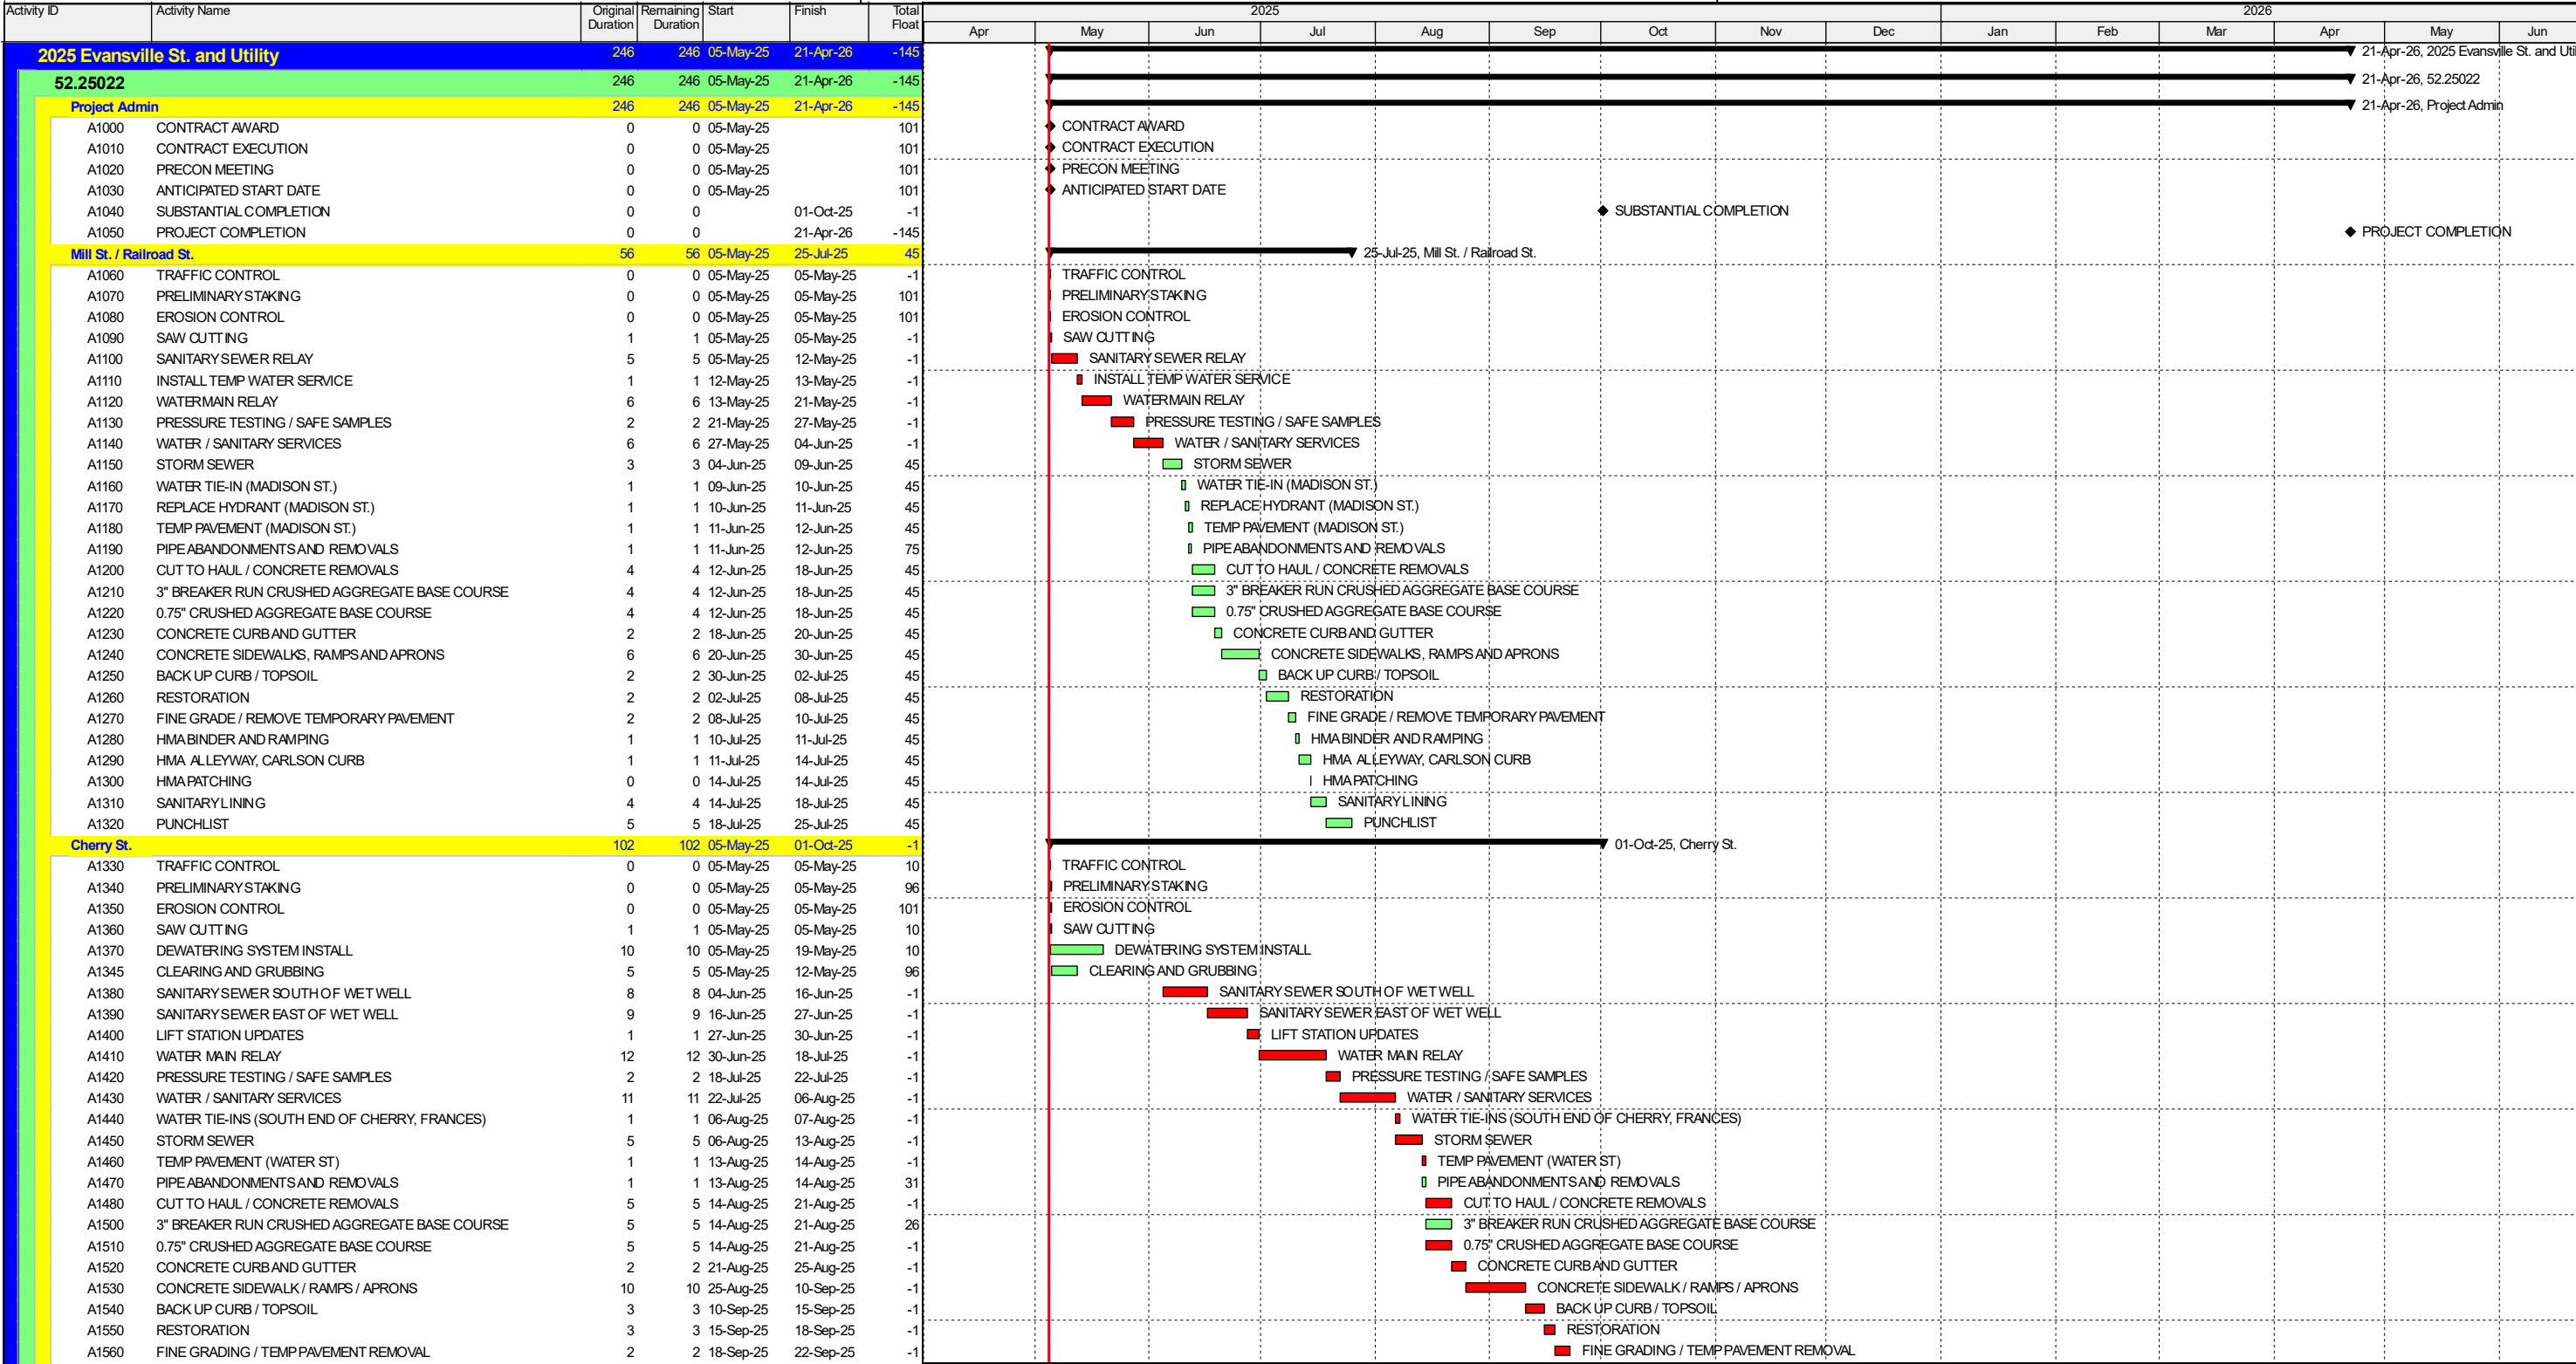

Actual Work Critical Remaining Work Summary
Remaining Work Milestone

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float	2025												2026					
							Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun			
A1570	HMA BINDER AND RAMPING	1	1	22-Sep-25	23-Sep-25	-1																		
A1580	HMA ALLEYWAY	1	1	23-Sep-25	24-Sep-25	-1																		
A1590	HMA PATCHING	0	0	24-Sep-25	24-Sep-25	-1																		
A1600	PUNCHLIST	5	5	24-Sep-25	01-Oct-25	-1																		
Church St. Parking Area		25	25	05-May-25	10-Jun-25	76																		
A1610	TRAFFIC CONTROL	0	0	05-May-25	05-May-25	76																		
A1620	EROSION CONTROL	0	0	05-May-25	05-May-25	101																		
A1630	PRELIMINARY STAKING	1	1	05-May-25	05-May-25	76																		
A1640	STORM SEWER	3	3	05-May-25	08-May-25	76																		
A1650	CUT TO HAUL / REMOVALS	3	3	08-May-25	13-May-25	76																		
A1660	3" BREAKER RUN CRUSED AGGREGATE BASE COURSE	3	3	08-May-25	13-May-25	76																		
A1670	0.75" CRUSHED AGGREGATE BASE COURSE	3	3	08-May-25	13-May-25	76																		
A1680	CONCRETE CURB AND GUTTER	2	2	13-May-25	15-May-25	76																		
A1690	CONCRETE SIDEWALK / APRONS / RAMPS	6	6	15-May-25	27-May-25	76																		
A1700	BACK UP CURB / TOPSOIL	1	1	27-May-25	28-May-25	76																		
A1710	RESTORATION	1	1	28-May-25	29-May-25	76																		
A1720	FINE GRADING	1	1	29-May-25	30-May-25	76																		
A1730	HMA SURFACE	1	1	30-May-25	02-Jun-25	76																		
A1740	PAVEMENT MARKING	1	1	02-Jun-25	03-Jun-25	76																		
A1750	PUNCHLIST	5	5	03-Jun-25	10-Jun-25	76																		
Brown School Road		16	16	05-May-25	28-May-25	85																		
A1760	TRAFFIC CONTROL	0	0	05-May-25	05-May-25	92																		
A1770	PRELIMINARY STAKING	0	0	05-May-25	05-May-25	92																		
A1780	SAW CUTTING	0	0	05-May-25	05-May-25	92																		
A1790	CUT TO HAUL / REMOVALS	1	1	13-May-25	14-May-25	85																		
A1800	0.75" DGB	1	1	13-May-25	14-May-25	85																		
A1810	CONCRETE CURB AND GUTTER	1	1	14-May-25	15-May-25	85																		
A1820	CONCRETE SIDEWALK / APRONS / RAMPS	5	5	15-May-25	22-May-25	85																		
A1830	TOPSOIL	1	1	22-May-25	27-May-25	85																		
A1840	RESTORATION	1	1	27-May-25	28-May-25	85																		
Garfield Ave Sidewalk		16	16	05-May-25	28-May-25	85																		
A1850	TRAFFIC CONTROL	0	0	05-May-25	05-May-25	92																		
A1860	PRELIMINARY STAKING	0	0	05-May-25	05-May-25	92																		
A1870	CLEARING AND GRUBBING	1	1	05-May-25	05-May-25	92																		
A1880	CUT TO HAUL / REMOVALS	1	1	14-May-25	15-May-25	85																		
A1890	0.75" DGB	1	1	14-May-25	15-May-25	85																		
A1900	CONCRETE SIDEWALK / APRONS / RAMPS	5	5	15-May-25	22-May-25	85																		
A1910	TOPSOIL	1	1	22-May-25	27-May-25	85																		
A1920	RESTORATION	1	1	27-May-25	28-May-25	85																		
2026 Split Sequence Paving		2	2	20-Apr-26	21-Apr-26	-145																		
A1930	Cherry St. Mill Ramps	1	1	20-Apr-26*	20-Apr-26	-145																		
A1950	Mill / Railroad St. Mill Ramps	1	1	20-Apr-26	20-Apr-26	-145																		
A1940	Cherry St HMA Surface	1	1	21-Apr-26	21-Apr-26	-145																		
A1960	Mill / Railroad St. HMA Surface	1	1	21-Apr-26	21-Apr-26	-145																		
